

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 034
Date: 2014-10-03
Day: Friday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Wayne R. Lawson, P.E.

Contractor: G.V.W., Inc.

Weather: 8:30 am: clear **Noon:** sunny **4:00 pm:**
Temperature: 8:30 am: 50° **Noon:** 68° **4:00 pm:**

Superintendent:

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General	Div. 06		Carpenter	1	0	2	3
Contractor:	Div. 04	GVW	Masonry	1	0	0	1
	09 90 00		Painting	0	0	0	0
	02 41 19		Demolition	1	0	9	10

Subcontractors:

Total:	3	0	11	14
---------------	----------	----------	-----------	-----------

DAILY REPORT

Activities Today:

- 1). Carpenters working on shoring installation in the 1st floor.
- 2). Demolition is ongoing at the balcony and basement.
- 3). Mason is cutting mortar joints at the front elevation of the building.
- 4). Lumber was delivered to the site.

Copies to: Richard Montuori, Town of Tewksbury
Ed Johnson, Town of Tewksbury Building Department
Steve Sadwick, Town of Tewksbury Building Department
Wayne Lawson, CBI
Jenne dos Santos, CBI
Kaffee Kang, Kang Architects


PHOTO INDEX



Temporary shoring has been erected at the 1st floor to support the 2nd floor.



Mezzanine at the Main Hall has been demolished.

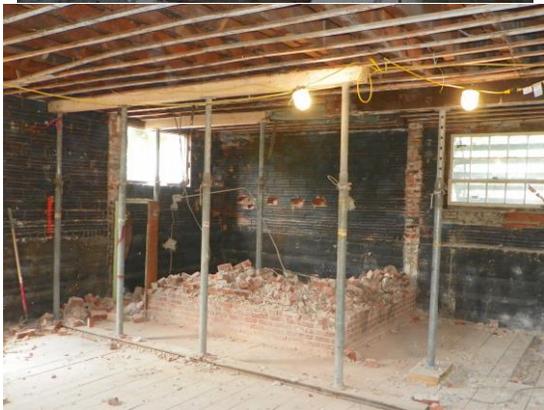

Temporary shoring has been installed in the basement and the brick masonry walls are being removed.



Mason is cutting mortar joints at the front elevation of the building in preparation for repointing.



Framing lumber was delivered to the site and is stored within the construction zone at the front of the building.
