

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
 Report No. 61
 Date: 2014-11-13
 Day: Thursday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Wayne R. Lawson, P.E., SECB

Contractor: G.V.W., Inc.

Weather: 7:30 am: Clear **Noon:** Clear **3:00 pm:** NA
Temperature: 7:30 am: 42° **Noon:** 45° **3:00 pm:** NA

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div.06	GVW	Carpenter	1	0	4	5
Subcontractors:	Div. 04	GVW	Masonry	1	0	3	4
	09 90 00	GVW	Painting	0	0	0	0
	02 41 19		Demolition	0	0	4	4
	Div. 31		Earthwork	1	0	1	2
	02 08 00	A&J Demos Services	Asbestos Abatement	1	0	1	2
	26 00 00	Griffin Electric	Electrician	0	0	0	0
	22 00 00	Lapan Mechanical	Plumber	0	0	0	0
		Steel	Iron Worker	1	0	0	1
	03 30 00	Precision Concrete	CIP Concrete	0	0	0	0
	07 31 00	Meadows Construction	Synthetic Slate Shingles	1	0	4	5
Total:				6	0	17	23

DAILY REPORT

Activities Today:

- 1) Carpenters are continuing to install new connectors for ceiling and attic framing over main hall.
- 2) Laborers are demolishing existing concrete slab in boiler room.
- 3) Workers are continuing with the demolition of the front entry ramps.
- 4) Abatement contractor is completing the removal of the faux roof slates.
- 5) Iron worker is on site performing field measurements and coordinating transport of new W18 beams into the building.
- 6) Roofing subcontractor is continuing with the installation of the synthetic slate shingles at the roof over the main hall.

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury Building Department
Steve Sadwick, Town of Tewksbury Building Department
Jeff Barnes, CBI
Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects


PHOTO INDEX



Demolition of front entry stairs and ramps is continuing.



Portion of the existing entry ramp that has been demolished.

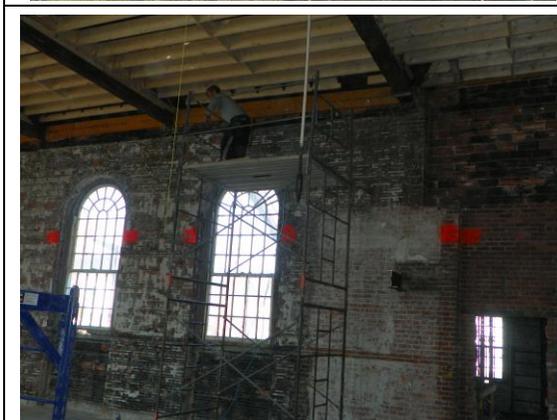


Installation of new metal connectors for ceiling and attic framing above the main hall is continuing.



Mason is continuing to cut out exterior mortar joints.



Removal of faux slate at roof over main hall has been completed.

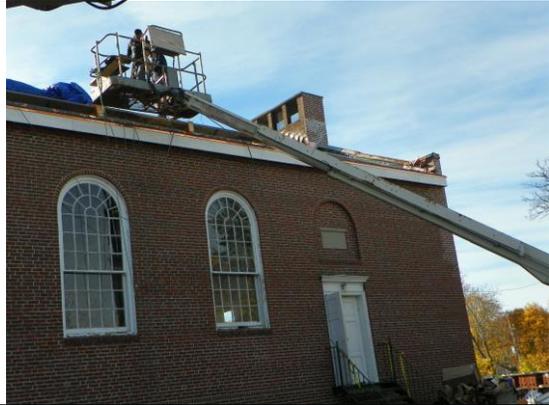

Installation of new synthetic slate shingles at roof over main hall is continuing.



New steel beam being transported into the building with lull for subsequent installation to support low roof.
