


TEWKSBURY WTF IMPROVEMENTS PROJECT

Weekly Progress Report for Week Ending: January 22, 2016

Design Engineer: AECOM
General Contractor: Kinsmen Corporation

I. Work Performed Last Week:

- The crews continued to work around the new generator pad; preparing the area for the concrete walkways around the pad.
- The crews removed both the carbon and sand from Filter No. 1. The crews started dis-assembly of the existing filter divider cell components. The crew also started the preliminary removal of the filter porous plates.

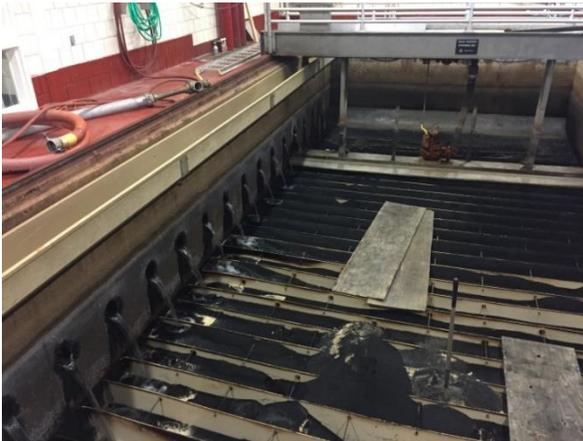

Preparation of carbon removal in Filter No. 1.



Carbon removal in Filter No. 1.



Sand removal in Filter No. 1.



Preparation of generator walkway subsoils.

II. Construction / Public Relation Issues:

- The contractor was reminded to maintain a safe work environment.

III. Erosion and Sedimentation Control:

- The contractor maintained the silt sock placed at the bottom of the front slope.
- Erosion control will be monitored and maintained throughout the project.

IV. Upcoming Work for Next Week:

- Remove the porous plates and the cell divider components from Filter No. 1.
- Tree removal behind the new generator pad.

V. Notes:

- Progress Meeting No. 2 is tentatively scheduled for Thursday (2/4/16).

Ted Angelakis
AECOM Resident Representative
