

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 010
Date: 2014-08-29
Day: Friday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: clear

Temperature: 7:30 am: 51°

Noon: partly cloudy

Noon: 70°

3:00 pm: partly cloudy

3:00 pm: 75°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman Super	Journeyman	Helpers	Total
General Contractor:		GVW	Carpenter	1	0	0	1
Subcontractors:	07 10 10	Chapman	Masonry	0	0	0	0
	09 90 90	Bello	Painting	0	0	0	0
	02 08 00	A & J Demo Services	Asbestos Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrician	1	0	1	2
Total:				2	0	1	3

DAILY REPORT

Activities today:

Electrician showed up this morning to review getting power to the trailer. This will require trenching from the building to the trailer to bring in the required power load. With this in mind, the electrician will be back on site next Wednesday to start that work.

GVW will arrange for equipment and manpower to trench and excavate for the electrician next Tuesday/Wednesday.

The sprinklers on the north side and in the plantings in front of the building are still operational. These will need to be shut down early next week.

The dumpster that the Town ordered was delivered this morning.

Copies to: Richard Montuori, Town of Tewksbury
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI
Jenne dos Santos, CBI
Kaffee Kang, Kang Architects

PHOTO INDEX



Photo showing sprinklers on the north elevation in operation.

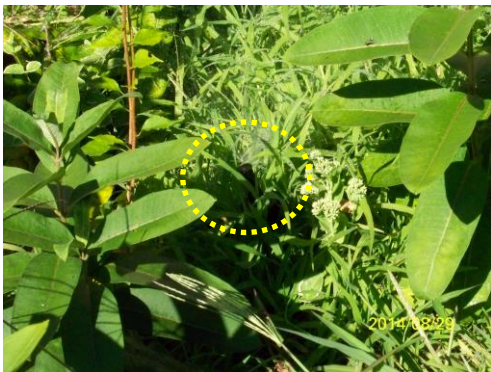


Photo showing sprinkler in the planting bed in front of the building. This is in operation and needs to be shut down as well.



Photo showing the town's dumpster in place.
