

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 023
Date: 2014-09-18
Day: Thursday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: sunny
Temperature: 7:30 am: 44°

Noon: sunny
Noon: 69°

3:00 pm: sunny
3:00 pm: 70°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	0	1	2
	Div. 04		Masonry	0	0	0	0
	09 90 00		Painting	0	0	0	0
	02 41 19		Demolition	1	0	6	7
Subcontractors:	02 08 00	A & J Demo Services	Asbestos Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrician	0	0	0	0
	22 00 00	Lapan Mechanical	Plumber	0	0	0	0
Total:				2	0	7	9

DAILY REPORT

Activities Today:

- 1) Started demo of the south wing, first floor by removing the ceiling and carpeting.
- 2) Removed a section of the gutter, fascia and soffit on the north elevation.
- 3) Removing floor boards from the basement.
- 4) Removing flooring and walls from north wing.

Copies to: Richard Montuori, Town of Tewksbury
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI
Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects

PHOTO INDEX



Photo showing flooring demo in the basement.



Photo showing the basement floor looking east.



Photo showing demo underway in the north wing, first floor.



Photo showing north wing demo in progress.



Photo showing carpenter working on mock-up for new fascia and soffit.

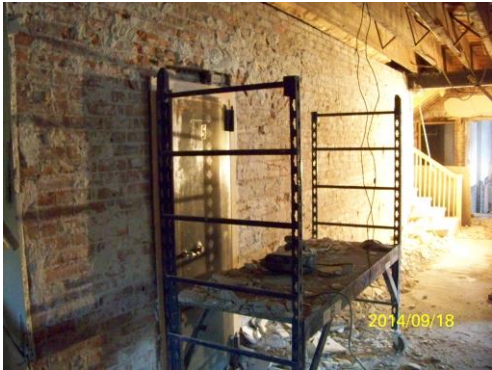


Photo showing plaster removed from one wall in the basement hallway.



Photo showing storage room in basement with the ceiling removed.
