

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 098
Date: 2015-01-09
Day: Friday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: cloudy
Temperature: 7:30 am: 22°

Noon: partly sunny
Noon: 24°

3:00 pm: partly sunny
3:00 pm: 28°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	2	0	3
	Div. 04		Masonry	1	0	0	1
	09 90 00		Painting	0	0	0	0
	02 41 19		Demolition	1	2	1	4
	Div. 31		Site Work	0	0	0	0
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	1	1	2	4
Subcontractors:	02 08 00	A & J Demo Services	Asbestos Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrician	0	0	0	0
	22 00 00	Lapan Mechanical	Plumber	0	0	0	0
	07 31 00	Meadows Construction	Synthetic Slate Shingles	0	0	0	0
	Div. 23	Ambient Temp. Corp.	HVAC	1	0	1	2
	Div. 21	Encore Fire Protection	Fire Suppression	1	0	1	2
Total:				6	5	5	16

DAILY REPORT

Activities Today:

- 1) Mason: working on new doorway in the basement
- 2) Demo/Labor: general site cleaning; assisting other trades; wet curing vault slab and covering it
- 3) Carpenter: working on threshold and floor tie-ins between the meeting hall floor and north and south wings; continuing with tie-backs along the east elevation of the main building
- 4) Fire Suppression: continuing with sprinkler installation in the attic
- 5) HVAC: continuing with ductwork and equipment installation in the attic
- 6) Concrete: finishing up reinforcement installation for inspection by Briggs; placing concrete for elevator pit and footings for addition; placing mesh reinforcement for main basement floor

Copies to: Richard Montuori, Town of Tewksbury
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI
Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.

PHOTO INDEX



Photo showing carpenter installing tie-backs along the roof line of the main building.



Photo showing carpenter working on the floor lines between the meeting hall and the south wing.



Photo showing crew getting ready for concrete placement for the elevator pit and footings.



Photo showing concrete being placed.



Another photo of concrete placement. The workman to the left of the chute is torching off any moisture prior to the concrete being placed in that section.



Photo showing more ductwork being installed in the attic.

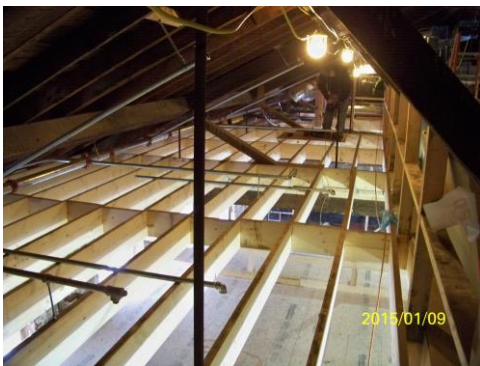


Photo showing the sprinkler lines being installed in the attic.



Photo showing the vapor barrier being taped prior to placing the mesh reinforcement.



Photo showing the mesh being placed.



Photo showing the mesh in place and supports being installed.



Photo showing workman covering the vault slab after wetting it down for curing.
