

# PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1  
Report No. 118  
Date: 2015-02-09  
Day: Monday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. Clerk of the Works: Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: snow  
Temperature: 7:30 am: 14°

Noon: snow  
Noon: 15°

3:00 pm: snow  
3:00 pm: 16°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	4	1	6
	Div. 04		Masonry	1	0	0	1
	09 90 00		Painting	0	0	0	0
	02 41 19		Demolition	1	1	0	2
	Div. 31		Site Work	0	0	0	0
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	0	0	0	0
Subcontractors:	02 08 00	A & J Demo Services	Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrical	0	0	0	0
	22 00 00	Lapan Mechanical	Plumbing	1	0	1	2
	07 31 00	Meadows Construction	Roofing	0	0	0	0
	07 53 00						
	07 61 19	Ambient Temp. Corp.	HVAC	1	0	1	2
	Div. 23						
	Div. 21	Encore Fire Protection	Fire Suppression	0	0	0	0
Total:				5	5	3	13

## DAILY REPORT

### Activities Today:

- 1) Carpenter: continuing with stud wall framing for 1<sup>st</sup> and 2<sup>nd</sup> floors; continuing framing for stair #2; laying out walls for the 1<sup>st</sup> floor – north wing; laying out bathroom walls in the basement; laying out walls on the 2<sup>nd</sup> floor of the main building; working on framing for platform at west end of meeting hall
- 2) HVAC: continuing with equipment installation and ductwork for 1<sup>st</sup> floor – south wing
- 3) Mason: working on masonry openings for windows on the 2<sup>nd</sup> floor – north elevation
- 4) Plumbing: continuing with piping installation for the 1<sup>st</sup> floor and basement; installing roof drain lines on the south roof
- 5) Demo/Labor: snow removal operations

Copies to: Richard Montuori, Town of Tewksbury  
Ed Johnson, Town of Tewksbury  
Steve Sadwick, Town of Tewksbury  
Wayne Lawson, CBI

Jenne dos Santos, CBI  
Kaffee Kang, Kang Architects  
Jennifer Pincus, Kang Architects  
Bob Harukewicz, GVW Inc.

# PHOTO INDEX



Photo showing carpenter laying out wall locations on the 2<sup>nd</sup> floor of the main building.



Photo showing carpenter cutting out stringers for stair #2.



Photo showing the progression of stair #2.



Photo showing stair #2 getting treads and riders framed in.



Photo showing carpenters framing the south end of the platform for the west end of the meeting hall.



Photo showing carpenter installing wall studs for the 1<sup>st</sup> floor north wing.



Photo showing wall tracks in place for the basement bathrooms.



Photo showing plumbers working on the roof drain line on the south wing.



Photo showing tin knocker installing ductwork for the south wing.

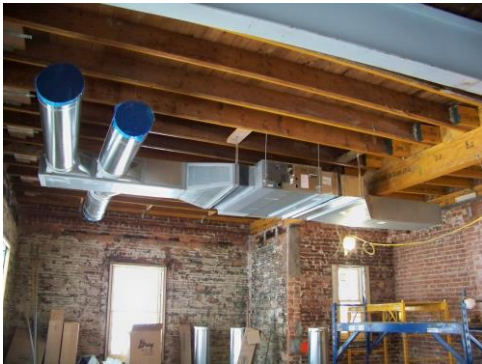


Photo showing some of the HVAC work in place in the north wing.
