

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 150
Date: 2015-03-26
Day: Thursday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jennifer dos Santos, Assoc. AIA, MCPPO

Contractor: G.V.W., Inc.

Weather: 7:30 am: Clear/ Sunny
Temperature: 7:30 am: 41°

Noon: Clear/ Sunny
Noon: 50°

3:00 pm: Clear/ Sunny
3:00 pm: 52°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	8	0	9
	Div. 04		Masonry	0	0	0	0
	09 90 00		Painting	1	0	0	1
	02 41 19		Laborers	1	2	0	3
	Div. 31		Site Work	0	0	0	0
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	0	0	0	0
Subcontractors:	02 08 00	A & J Demo Services	Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	1	0	0	1
	03 30 00	L&L Concrete	Concrete	0	0	0	0
	Div. 23	Ambient Temp. Corp.	HVAC	1	4	1	6
	Div. 21	Encore Fire Protection	Fire Suppression	1	1	0	2
Total:				7	16	1	24

DAILY REPORT

Activities Today:

- 1) **Carpenters:** installing caulking around windows, framing the coffered ceilings, installing drywall in Storage Room #107, framing soffits in basement and performing soffit and coffer layout in the basement and 1st floor.
- 2) **Painter:** Painting lintels, and taping Electrical Room drywall.
- 3) **Laborers:** Performing general site clean-up and assisting other trades and installing waterproofing and protection board on the new foundation.
- 4) **HVAC:** Installing rough piping on the 1st and ground floor, copper pipe insulation is being installed on the 1st floor.
- 5) **Griffin Electric:** Installing rough electrical in the basement.
- 6) **Plumbing:** Installing fire caulking at floor penetrations at the 1st and 2nd floors.


Copies to: Richard Montuori, Town of Tewksbury
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jeff Barnes, Barnes Consulting
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.

PHOTO INDEX



HVAC workers continue installing rough piping.

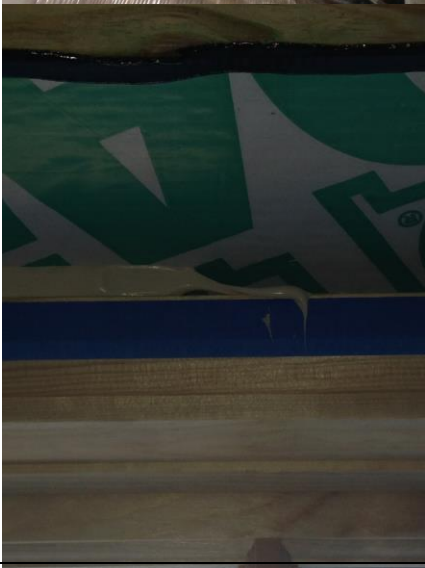

Window caulking is being installed in the basement.



Coffered ceiling framing continues in the Meeting Room.
