

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 152
Date: 2015-03-30
Day: Monday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: cloudy
Temperature: 7:30 am: 32°

Noon: light flurries
Noon: 35°

3:00 pm: cloudy
3:00 pm: 40°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	4	1	6
	Div. 04		Masonry	0	0	0	0
	09 90 00		Paint/Plaster	1	0	0	1
	02 41 19		Labor	1	0	0	1
	Div. 31		Site Work	1	2	0	3
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	0	0	0	0
	07 21 00		Insulation	0	0	0	0
Subcontractors:	02 08 00	A & J Demo Services	Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	0	0	0	0
	07 31 00	Meadows Construction	Roofing	0	0	0	0
	07 53 00						
	07 61 19	Ambient Temp. Corp.	HVAC	2	5	1	8
	Div. 23						
Total:	Div. 21	Encore Fire Protection	Fire Suppression	0	0	0	0
				7	12	2	21

DAILY REPORT

Activities Today:

- 1) Carpentry: starting to hang ceilings on the 2nd floor; continuing with framing out the soffits in the meeting hall;
- 2) Electrical: continuing with wiring in the basement
- 3) HVAC: continuing with mechanical piping and equipment installation; continuing with insulating ductwork and piping; continuing with control wiring installation
- 4) Labor: general site cleaning; assisting other trades;
- 5) Site Work: starting backfilling and compaction operations at the addition around the footings and foundations. Briggs Testing is on site to perform compaction testing. Briggs will return tomorrow to complete the testing.
- 6) Paint/Plaster: taping and mudding the storage room on the south end of the platform

PHOTO INDEX



Photo showing carpenters installing GWB for the ceiling on the 2nd floor.



Photo showing carpenter installing GWB on the 2nd floor ceiling.



Photo meeting hall ceiling framing taking shape. This is looking at the west end of the meeting hall.

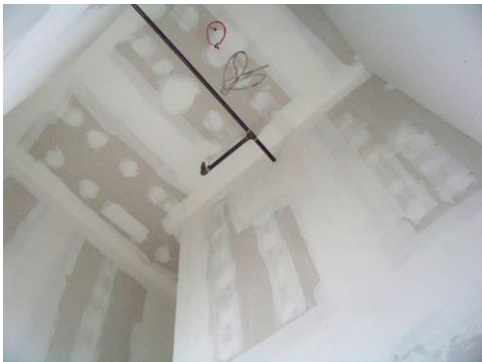


Photo showing the roughed in closet at the north end of the platform in the meeting hall.



Photo showing plasterer working in the storage room at the south end of the platform in the meeting hall.



Photo showing HVAC workman making room for control wiring.



Photo showing HVAC mechanic installing control wiring in the basement.



Photo showing electrician continuing with the wiring installation.



Photo showing foundation wall with waterproofing and protection board (blue) installed, and insulation installed (pink).



Photo showing workmen prepping the soil to get ready for compacting.



Photo showing the compaction machine and the area after being compacted.



Photo showing soil being dumped for backfilling.

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.
