

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 157
Date: 2015-04-06
Day: Monday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: cloudy
Temperature: 7:30 am: 34°

Noon: cloudy
Noon: 45°

3:00 pm: some sun
3:00 pm: 51°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	4	1	6
	Div. 04		Masonry	1	0	1	2
	09 90 00		Paint/Plaster	1	0	0	1
	02 41 19		Labor	1	0	0	1
	Div. 31		Site Work	1	1	0	2
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	1	0	0	1
	07 21 00		Insulation	0	0	0	0
Subcontractors:	02 08 00	A & J Demo Services	Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	0	0	0	0
	07 31 00	Meadows Construction	Roofing	0	0	0	0
	07 53 00						
	07 61 19						
	Div. 23	Ambient Temp. Corp.	HVAC	2	3	1	6
	Div. 21	Encore Fire Protection	Fire Suppression	0	0	0	0
Total:				9	9	3	21

DAILY REPORT

Activities Today:

- 1) Carpentry: continuing to hang GWB on the walls and ceilings on the 2nd floor; continuing to frame the ceiling and soffits in the meeting hall; continuing with framing soffits in the basement; installing blocking for handrails on stairs 2 and 3; starting to install insulation in the attic; starting to hang GWB ceiling in the basement
- 2) Electrical: continuing with in-wall rough installation on all floors
- 3) HVAC: continuing with mechanical piping and equipment installation on all floors; continuing with insulation of piping on all floors; testing parts of the system
- 4) Labor: general site cleaning; assisting other trades
- 5) Site Work: back filling and compacting soil in area beneath the vault in the addition
- 6) Concrete: installing rebar cages and formwork for the entryway slab grade beams
- 7) Masonry: starting to block in the doorway in the basement on the west wall adjacent to the addition

PHOTO INDEX



Photo showing compacting in progress in the area beneath the vault.



Photo showing the area where the rebar cages have been installed and the formwork erected.



Photo showing a workman coring holes for the trades to install piping for the addition.



Photo showing doorway that is to be blocked in.



Photo showing mason starting to block in the doorway.



Photo showing electrician running wiring in the basement.

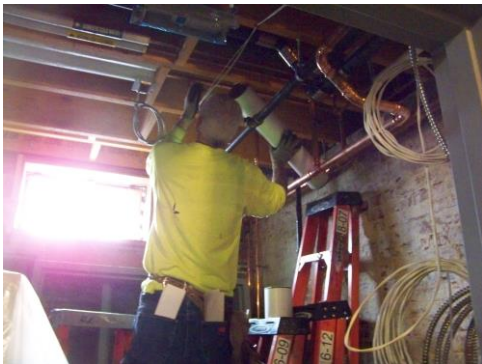


Photo showing workman installing insulation on piping in the basement.

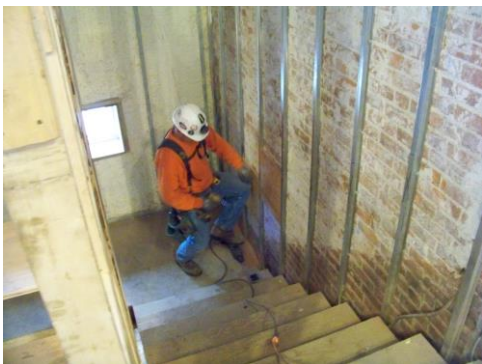






Photo showing carpenter installing blocking for handrails on stair #2.

	<p>Photo showing blocking in place for the handrails at stair #3.</p>
	<p>Photo showing carpenter installing GWB on the 2nd floor.</p>
	<p>Photo showing HVAC mechanic testing some of the piping used for heating.</p>
	<p>Photo showing the testing apparatus in place.</p>

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.
