

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 162
Date: 2015-04-13
Day: Monday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: clear

Temperature: 7:30 am: 36°

Noon: clear

Noon: 71°

3:00 pm: clear

3:00 pm: 72°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	5	1	7
	Div. 04		Masonry	1	0	0	1
	09 90 00		Paint/Plaster	1	0	0	1
	02 41 19		Labor	1	2	0	3
	Div. 31		Site Work	0	0	0	0
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	1	4	0	5
	07 21 00		Insulation	0	0	0	0
Subcontractors:	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	0	0	0	0
	07 31 00	Meadows Construction	Roofing	0	0	0	0
	07 53 00						
	07 61 19	Ambient Temp. Corp.	HVAC	2	3	1	6
	Div. 23						
	Div. 21	Encore Fire Protection	Fire Suppression	1	1	0	2
	13 27 16	Fire Lock	Modular Fire Vault	1	1	0	2
Total:				8	14	1	23

DAILY REPORT

Activities Today:

- 1) Carpentry: continuing with installation of blocking in the ceiling framing in the meeting hall; installing GWB on 1st floor – south wing; installing GWB on 1st floor – north wing; laying out blocking for memorial plaques on 1st floor; starting to install GWB in the lobby on the 1st floor
- 2) HVAC: continuing with mechanical piping and equipment installation on all floors; continuing with insulation of piping on all floors
- 3) Labor: general site cleaning; assisting other trades
- 4) Masonry: cutting out masonry openings and installing lintels in wall for the vault
- 5) Fire Vault: continuing with vault installation
- 6) Paint/Plaster: starting to tape and mud GWB joints on the 2nd floor
- 7) Concrete: entry slab, vault slab and lower level slab at the addition are being placed today; Briggs is on site for testing

PHOTO INDEX



Photo showing work crew ready for the concrete placement.



Photo showing concrete truck and pump truck in place, ready to go.



Photo showing concrete being placed for the vault slab.



Photo showing the finishing work taking place.



Photo showing workman sealing around the louvers on the east side of the chimney.



Photo showing GWB installed in the north wing of the 1st floor.



Photo showing the vault in the process of being assembled.



Photo showing a section of the vault wall.



Photo openings in the masonry wall for the vault.




Photo showing insulation being installed around ductwork and HVAC piping.



Photo showing a carpenter installing GWB on the 1st floor – south wing.



Photo showing carpenter laying out blocking in the wall for the memorial plaques.

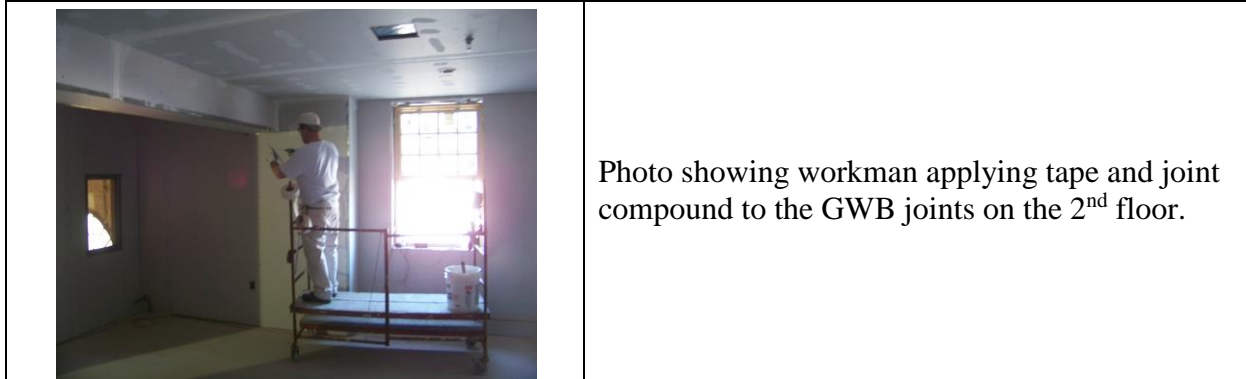

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.
