

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 174
Date: 2015-04-30
Day: Thursday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: partly cloudy
Temperature: 7:30 am: 46°

Noon: some sun
Noon: 57°

3:00 pm: cloudy
3:00 pm: 62°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	4	1	6
	Div. 04		Masonry	1	1	0	2
	09 90 00		Paint/Plaster	1	1	0	2
	02 41 19		Labor	1	2	0	3
	Div. 31		Site Work	0	0	0	0
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	0	0	0	0
	07 21 00		Insulation	0	0	0	0
Subcontractors:	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	0	0	0	0
	07 31 00	Meadows Construction	Roofing	0	0	0	0
	07 53 00						
	07 61 19	Ambient Temp. Corp.	HVAC	3	3	0	6
	Div. 23						
	Div. 21	Encore Fire Protection	Fire Suppression	0	0	0	0
Total:	13 27 16	Fire Lock	Modular Fire Vault	0	0	0	0
				8	12	1	21

DAILY REPORT

Activities Today:

- 1) Carpentry: continuing to install sheetrock in the basement; installing subfloor on 2nd floor
- 2) HVAC: installing vibration dampers; continuing with condensate drain lines; continuing with piping insulation; continuing with control wiring installation
- 3) Labor: general site cleaning; assisting other trades;
- 4) Masonry: laying block for the east wall of the addition
- 5) Paint/Plaster: taping and mudding stairwell 3; continuing to tape and mud the joints on the 1st floor
- 6) Electrical: continuing with lighting rough installation in the basement; installing floor boxes; continuing with rough wiring in the basement

PHOTO INDEX



Photo showing subfloor installed on the 2nd floor.

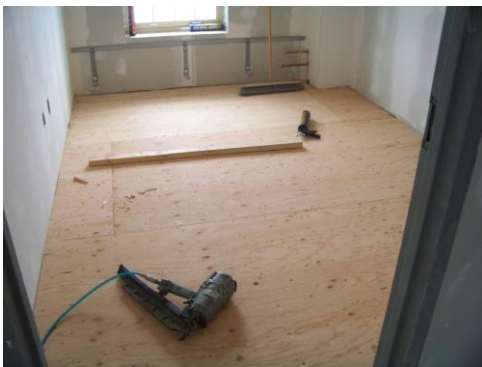


Photo showing subfloor in place on the 2nd floor.



Photo showing controls technician running wiring in the attic.



Photo showing one of the panels installed in the electrical room in the northwest corner of the meeting hall.



Photo showing sheetrock being taped and mudded on the 1st floor.



Photo showing masons installing CMU block for the addition.



Photo showing some of the CMU block installed with horizontal reinforcement in place.



Photo showing CMU block wall with flashing installed along the bottom.



Photo showing carpenter working in the downstairs break room.



Photo showing electrician installing floor boxes in the meeting hall.

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.
