

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
Report No. 182
Date: 2015-05-12
Day: Tuesday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. Clerk of the Works: Jennifer dos Santos, Assoc. AIA, MCPPO

Contractor: G.V.W., Inc.

Weather: 7:30 am: Overcast Noon: Mostly Sunny 3:00 pm: Sunny
Temperature: 7:30 am: 62° Noon: 72° 3:00 pm: 74°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	3	0	4
	Div. 04		Masonry	1	2	2	5
	09 90 00		Painting	1	0	0	1
	02 41 19		Laborers	1	0	0	1
	Div. 31		Site Work	1	2	0	3
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	0	0	0	0
Subcontractors:	02 08 00	A & J Demo Services	Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	0	0	0	0
	03 30 00	L&L Concrete	Concrete	0	0	0	0
	Div. 23	Ambient Temp. Corp.	HVAC	2	2	0	4
	Div. 21	Encore Fire Protection	Fire Suppression	0	0	0	0
	Div. 7	Meadows Roofing	Roofing	0	0	0	0
Total:				8	10	2	20

DAILY REPORT

Activities Today:

- 1) Carpenters: (1) is installing framing in the lobby, (1) installing drywall in Stair #2, (2) installing drywall at the platform in the Meeting Hall.
- 2) Laborers: water line installation (including one equipment operator).
- 3) Painter: painting the Electric Room and the Storage Room in the Meeting Hall.
- 4) Taper: taping drywall on the 1st floor.
- 5) HVAC: continuing insulation of the ductwork and piping in the attic; installing fin tube radiation heat.
- 6) Griffin Electric: continuing electrical rough installation and electrical wiring in the lobby and 1st floor.
- 7) Masons: installing CMU block at the addition with (2) mason tenders.


Copies to: Richard Montuori, Town of Tewksbury
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jeff Barnes, Barnes Consulting
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.

PHOTO INDEX



The water line installation continues.

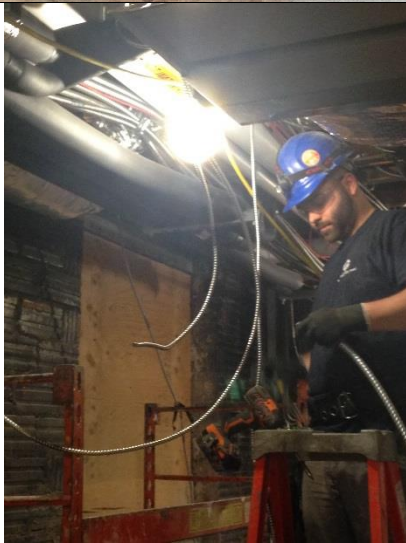

The electricians are installing rough electrical.



Carpenters are installing drywall at the platform in the Meeting Hall.



The first floor drywall is being taped.



The Electric Room and the Storage Room in the Meeting Hall have been painted.



The masons are continuing with the CMU block installation at the addition.
