

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
 Report No. 189
 Date: 2015-05-21
 Day: Thursday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: clear **Noon:** some clouds **3:00 pm:** some clouds
Temperature: 7:30 am: 49° **Noon:** 65° **3:00 pm:** 67°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	3	0	4
	Div. 04		Masonry	1	1	3	5
	09 90 00		Paint/Plaster	1	1	0	2
	02 41 19		Labor	1	2	0	3
	Div. 31		Site Work	0	0	0	0
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	0	0	0	0
	07 21 00		Insulation	0	0	0	0
Subcontractors:	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	0	0	0	0
	07 31 00	Meadows Construction	Roofing	1	3	0	4
	07 53 00						
	07 61 19	Ambient Temp. Corp.	HVAC	3	2	0	5
	Div. 23						
	Div. 21	Encore Fire Protection	Fire Suppression	0	0	0	0
Total:	13 27 16	Fire Lock	Modular Fire Vault	0	0	0	0
				9	13	3	25

DAILY REPORT

Activities Today:

- 1) Carpentry: installing sheetrock in the vault; installing plywood subfloor in the north wing
- 2) HVAC: continuing with HVAC piping insulation in the attic; making and installing sleepers for rooftop mechanical units on south wing; continuing with ductwork installation; continuing with control wiring installation
- 3) Labor: working with trades; general site cleaning;
- 4) Masonry: continuing with the installation of CMU blocks for the addition
- 5) Paint/Plaster: continuing with taping & mudding joints on the basement;
- 6) Electrical: continuing with installing power and lighting equipment on all floors
- 7) Roofing: installing tapered insulation on the south roof

PHOTO INDEX



Photo showing workman applying joint compound to a wall in the basement.



Photo showing wood sleepers in place on the south roof.



Photo showing plywood subfloor being installed on the 1st floor – north wing.



Photo showing roofers installing tapered insulation on the south wing roof.



Photo showing tin knocker installing a register in the ceiling.



Photo showing sheetrock installed in the vault.



Photo showing masons working on the CMU block for the addition.

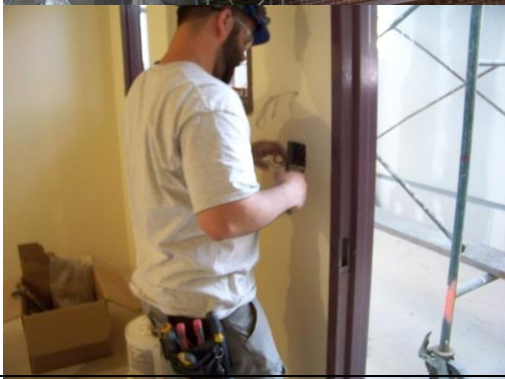


Photo showing electrician installing wiring for wall switch on the 1st floor.

	<p>Photo showing some of the light fixtures that have been installed.</p>
	<p>Photo showing some other light fixtures installed.</p>

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.
