



TEWKSBURY WTF IMPROVEMENTS PROJECT

Weekly Progress Report for Week Ending: February 19, 2016

Design Engineer: AECOM
General Contractor: Kinsmen Corporation

I. Work Performed Last Week:


- The crews completed the cleanup of the effluent channel for Filter No. 1 following the epoxy coating work.
- Several shipments were made to the site including the delivery of filter replacement parts. The contractor moved a portion of the materials into the plant in preparation for the filter re-assembly work scheduled to start the following week.
- The contractor installed the angle supports for the vertical cell dividers along the inside walls of Filter No. 1.
- The electrician completed the wiring for the temporary electrical transformer. The electrician also delivered a site trailer and started setting up the trailer.



Cleanup of effluent channel for Filter No. 1 following epoxy coating.



Shipment of replacement porous plates for Filter No. 1.

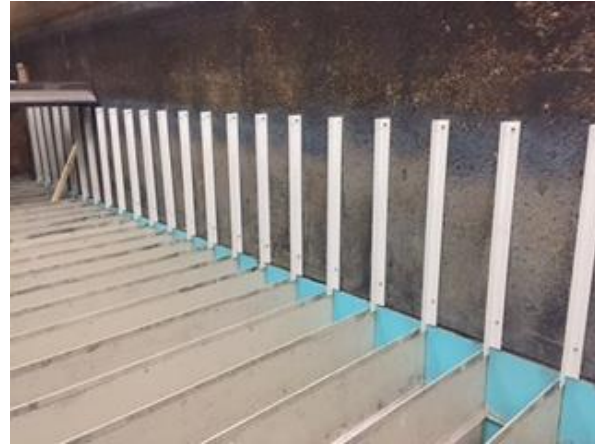

Installation of angle supports for vertical cell dividers.

II. Construction / Public Relation Issues:

- The contractor was reminded to maintain a safe work environment.

III. Erosion and Sedimentation Control:

- The contractor maintained the silt sock placed at the bottom of the front slope.
- Erosion control will be monitored and maintained throughout the project.

IV. Upcoming Work for Next Week:

- Electrical subcontractor mobilization.
- Filter No. 1 – Continue with the installation of the new components.
- Expected delivery of the remaining filter replacement parts.

V. Notes:

- The next monthly progress meeting is scheduled for Thursday, March 3, 2016.

Ted Angelakis
AECOM Resident Representative
