

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
 Report No. 02
 Date: 2014-08-19
 Day: Tuesday

Architect: Kang Associates
Project: Renovation and Addition to Tewksbury Town Hall
OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes
Contractor: G.V.W., Inc.

Weather: 7:30 am: Noon: clear 3:00 pm:
Temperature: 7:30 am: Noon: 74° 3:00 pm:

Superintendent:

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman Super	Journeyman	Helpers	Total
General Contractor:		GVW	Carpenter	1	0	0	1
Subcontractors:	07 10 10	Chapman	Masonry	0	0	0	0
	09 90 90	Bello	Painting	0	0	0	0
	02 08 00	A & J Demo Services	Asbestos Abatement	1	0	5	6
	31 10 00	Dakoda Tree Service	Arborist	0	0	0	0
	22 00 00	Lapan Mechanical	Plumber	0	0	0	0
Total:				2	0	5	7

DAILY REPORT

Work in progress:
 A & J Demo Services has (2) men working in the first floor covering doorways and windows, and four (4) men working in the attic removing insulation.
 GVW had the super on site reviewing the project layout and marking out areas for the silt fence, temp fencing and demo. Also reviewing the walls in the basement for demo approaches.

Copies to: **Richard Montuori, Town of Tewksbury**
Wayne Lawson, CBI
Jenne dos Santos, CBI
Kaffee Kang, Kang Architects

PHOTO INDEX



Photo showing the abatement contractor setting up the first floor for demo.

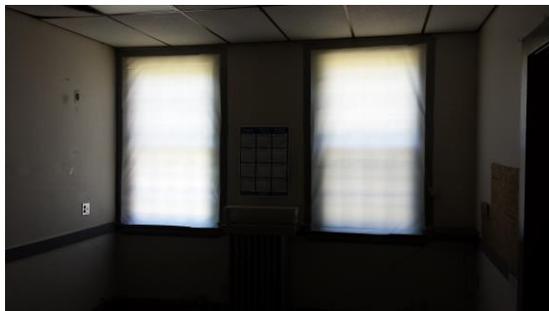


Photo showing windows covered over in preparation for demo on the first floor.



Photo showing some of the items to be removed during the demo. These were marked out by the GC.



Photo showing other items to be removed during the demo. The low stone wall, metal stairs and shed are marked.
