

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
 Report No. 029
 Date: 2014-09-26
 Day: Friday

Architect: Kang Associates
Project: Renovation and Addition to Tewksbury Town Hall
OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes
Contractor: G.V.W., Inc.

Weather: 7:30 am: some clouds **Noon:** clear **3:00 pm:** clear
Temperature: 7:30 am: 47° **Noon:** 68° **3:00 pm:** 71°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	0	1	2
	Div. 04		Masonry	0	0	0	0
	09 90 00		Painting	0	0	0	0
	02 41 19		Demolition	1	0	7	8
Subcontractors:	02 08 00	A & J Demo Services	Asbestos Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrician	0	0	0	0
	22 00 00	Lapan Mechanical	Plumber	0	0	0	0
Total:				2	0	8	10

DAILY REPORT

- Activities Today:
- 1) Carpenters are working on the south elevation of the meeting hall installing the framework for the new fascia and soffit. They are also working on the north elevation of the meeting hall, getting it ready for the framework.
 - 2) Demo is continuing on the second floor: the balcony is in the process of being demolished.
 - 3) Demo is continuing on the first floor at the underside of the balcony.
 - 4) The north stairwell is in the process of being demolished.
 - 5) The finish is being removed from beneath the windows in the meeting hall.
 - 6) The vaults on the first floor have been demolished.

Copies to: Richard Montuori, Town of Tewksbury
 Ed Johnson, Town of Tewksbury
 Steve Sadwick, Town of Tewksbury
 Wayne Lawson, CBI
 Jenne dos Santos, CBI
 Kaffee Kang, Kang Architects
 Jennifer Pincus, Kang Architects

PHOTO INDEX

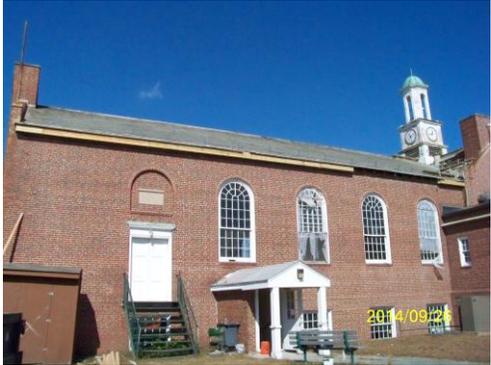


Photo showing the framework in place for the fascia and soffit on the south elevation.



Photo showing demolition of the balcony looking north.



Photo showing demolition of the balcony looking south.



Photo showing demo of the finish beneath the windows along the south elevation of the meeting hall.



Photo showing finishes being demolished along the north meeting wall.



Photo looking into the north stairwell from the second floor.



Photo showing a vault on the first floor completely demolished.



Photo looking into the south wing on the first floor.



Photo of a cross section of the second floor above the lobby.



Photo looking down into the lobby from the south stairs.
