

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
 Report No. 153
 Date: 2015-03-31
 Day: Tuesday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. **Clerk of the Works:** Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: clear **Noon:** clear **3:00 pm:** some clouds
Temperature: 7:30 am: 36° **Noon:** 44° **3:00 pm:** 47°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	5	1	7
	Div. 04		Masonry	0	0	0	0
	09 90 00		Paint/Plaster	1	0	0	1
	02 41 19		Labor	1	0	0	1
	Div. 31		Site Work	1	2	0	3
	01 50 00		Temp. Facility	0	0	0	0
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	0	0	0	0
	07 21 00		Insulation	0	0	0	0
Subcontractors:	02 08 00	A & J Demo Services	Abatement	0	0	0	0
	26 00 00	Griffin Electric	Electrical	1	1	0	2
	22 00 00	Lapan Mechanical	Plumbing	0	0	0	0
	07 31 00	Meadows Construction	Roofing	0	0	0	0
	07 53 00						
	07 61 19						
	Div. 23	Ambient Temp. Corp.	HVAC	2	3	1	6
Div. 21	Encore Fire Protection	Fire Suppression	0	0	0	0	
Total:				7	12	2	21

DAILY REPORT

Activities Today:

- 1) **Carpentry:** continuing to hang GWB ceilings on the 2nd floor; continuing with GWB wall installation on the 2nd floor; sealing around windows on the interior and exterior;
- 2) **Electrical:** continuing with wiring installation in the basement
- 3) **HVAC:** continuing with mechanical piping and equipment installation; continuing with insulating ductwork and piping
- 4) **Labor:** general site cleaning; assisting other trades
- 5) **Site Work:** continue backfilling and compaction operations around the footings and foundations. Briggs is on site to perform compaction testing.
- 6) **Paint/Plaster:** continuing taping and mudding the sheetrock walls on the 1st floor in the meeting hall storage room

PHOTO INDEX



Photo showing carpenter sealing the interior of a window in the clerk's office.



Photo showing carpenter sealing the exterior of a window on the north elevation of the north wing.

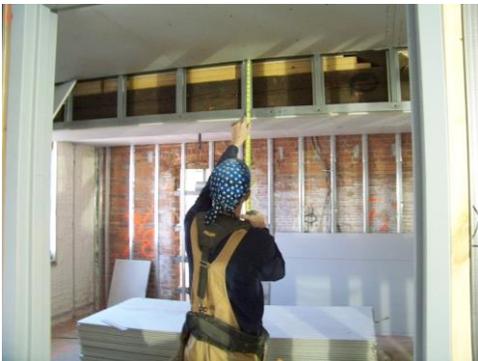


Photo showing carpenter installing sheetrock for a ceiling on the 2nd floor.



Photo showing carpenter installing sheetrock on ceiling on the 2nd floor.



Photo showing HVAC mechanics prepping area in the 1st floor lobby for piping installation.



Photo showing electrician running wire in the basement.



Photo showing HVAC mechanic connecting piping to one of the HVAC units.



Photo showing workman compacting backfilled soil and the technician from the testing company ready to test the soil.



Photo showing trench for below-grade drainage. The drain pipe and crushed stone has been placed.



Photo showing crushed stone being placed.



Photo showing drain pipe in place, leading to the foundation wall.



Photo showing area at addition with compacted soil.

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.
