

PROJECT REPRESENTATIVE'S DAILY REPORT

Pg. 1
 Report No. 250
 Date: 2015-08-17
 Day: Monday

Architect: Kang Associates

Project: Renovation and Addition to Tewksbury Town Hall

OPM: CBI Consulting Inc. Clerk of the Works: Jeff Barnes

Contractor: G.V.W., Inc.

Weather: 7:30 am: clear Noon: mostly sunny 3:00 pm: mostly sunny
 Temperature: 7:30 am: 69° Noon: 85° 3:00 pm: 92°

Superintendent: Vinnie Bomal

PERSONNEL COUNT	Spec Section	Contractor	Trade	Foreman	Journeyman	Helpers	Total
General Contractor:	Div. 06	GVW	Carpentry	1	1	0	2
	Div. 04		Masonry	0	0	0	0
	09 90 00		Paint/Plaster	1	0	0	1
	02 41 19		Labor	1	0	0	1
	Div. 31		Site Work	1	0	0	1
	Div. 05		Misc. Metals	0	0	0	0
	Div. 03		Concrete	0	0	0	0
	09 51 23		Drop Ceiling	0	0	0	0
	09 30 00		Tiling	0	0	0	0
Subcontractors:	26 00 00	Griffin Electric	Electrical	0	0	0	2
	22 00 00	Lapan Mechanical	Plumbing	1	0	0	1
	07 31 00	Meadows Construction	Roofing	0	0	0	0
	07 53 00						
	07 61 19						
	Div. 23	Ambient Temp. Corp.	HVAC	0	0	0	0
	Div. 21	Encore Fire Protection	Fire Suppression	1	1	0	2
	13 27 16	Fire Lock	Modular Fire Vault	0	0	0	0
	Div. 14	United Elevator	Elevator	0	0	0	0
	08 12 00	TCI	Doors	1	2	1	4
	08 14 00						
	08 14 23						
Total:				7	4	1	12

DAILY REPORT

Activities Today:

- 1) Carpentry: continuing with subfloor installation at the top of stairwell #1; installing last door and transom in lobby
- 2) Labor: assisting trades; general site cleaning
- 3) Site Work: continuing with rough grading of the site; backfilling at foundation infill; applied damp proofing to concrete infill
- 4) Fire Suppression: continuing with sprinkler installation at various locations throughout the building
- 5) Paint/Plaster: continuing with painting in the stairwell of the addition
- 6) Doors: continuing with installation of wood doors
- 7) Plumbing: installing bathroom appliances
- 8) Misc.: National Grid is on site connecting transformer

PHOTO INDEX



Photo showing workmen installing hinges on the wood doors to be installed.



Photo showing workman installing hardware on door to Town Manager's office.



Photo showing lobby doors.



Photo showing carpenter installing subfloor at top of stair #1.



Photo showing carpenters installing the framework for the last lobby door.



Photo showing toiler installed in a first floor bathroom.



Photo looking down Town Hall towards Dewey St. The National Grid crew is connecting the lines on the pole to the underground conduits that were placed previously.

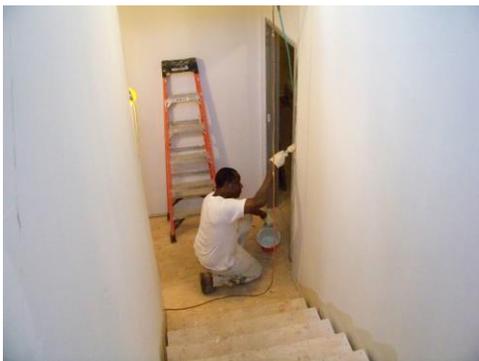


Photo showing painter working in the stairwell of the addition.

Copies to: **Richard Montuori, Town of Tewksbury**
Ed Johnson, Town of Tewksbury
Steve Sadwick, Town of Tewksbury
Wayne Lawson, CBI

Jenne dos Santos, CBI
Kaffee Kang, Kang Architects
Jennifer Pincus, Kang Architects
Bob Harukewicz, GVW Inc.
