


TEWKSBURY WTF IMPROVEMENTS PROJECT

Weekly Progress Report for Week Ending: April 1, 2016

Design Engineer: AECOM
General Contractor: Kinsmen Corporation

I. Work Performed Last Week:

- A representative from Aqua Aerobics was onsite to conduct a light test on the new porous plates installed at the bottom of Filter No. 2. The representative also inspected the porous plate installation and found no defects or leaks.
- The crews completed the installation of the upper cell dividers in Filter No. 2.
- The crews completed the mechanical and electrical upgrades to the Filter No. 2 bridge assembly.
- The crews welded the new travelling bridge rail caps on the bridge tracks.
- The electricians continued with the installation of the fire alarm conduit components on the walls and ceilings in the Filter Room No. 1 and 2.
- The electricians also completed the electrical terminations in the new generator.

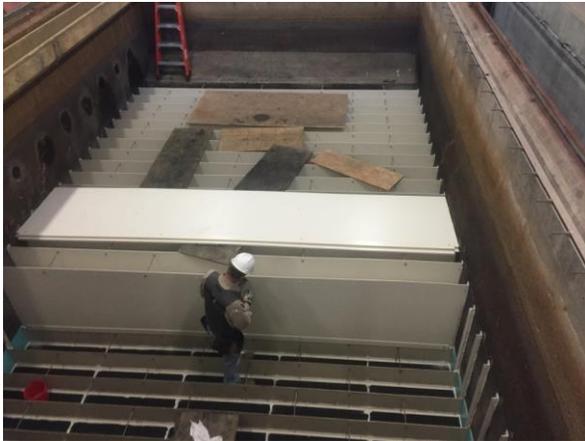


Upper cell divider installation for Filter No. 2



Completed installation of upper cell dividers in Filter No. 2



New welded bridge track cap for travelling bridge assembly.

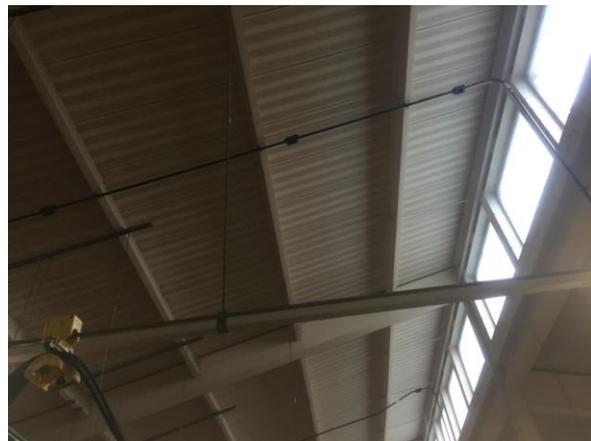

Fire alarm conduit installation along ceiling of Filter Room 1 & 2.



New drive components for Filter No. 2 travelling bridge assembly.

II. Construction / Public Relation Issues:

- The contractor was reminded to maintain a safe work environment.

III. Erosion and Sedimentation Control:

- The contractor maintained the silt sock placed at the bottom of the front slope.
- Erosion control will be monitored and maintained throughout the project.

IV. Upcoming Work for Next Week:

- Filter No. 2 – Effluent channel coating
- Filter No. 2 – Cleanup
- Filter No. 1/2 – Fire alarm electrical

V. Notes:

- The next progress meeting is scheduled for Thursday, April 7, 2016.

Ted Angelakis
AECOM Resident Representative
